


SEQUENCE COMMISSIONING AND START-UP DESALINATED WATER SUPPLY FOR SPENCE GROWTH OPTIONS PROJECT

NO ENERGY / NO CHARGE
CONSTRUCTION COMPLETION

WITH ENERGY / NO CHARGE
PRECOMMISSIONING

WITH ENERGY / WITH CHARGE
COMMISSIONING

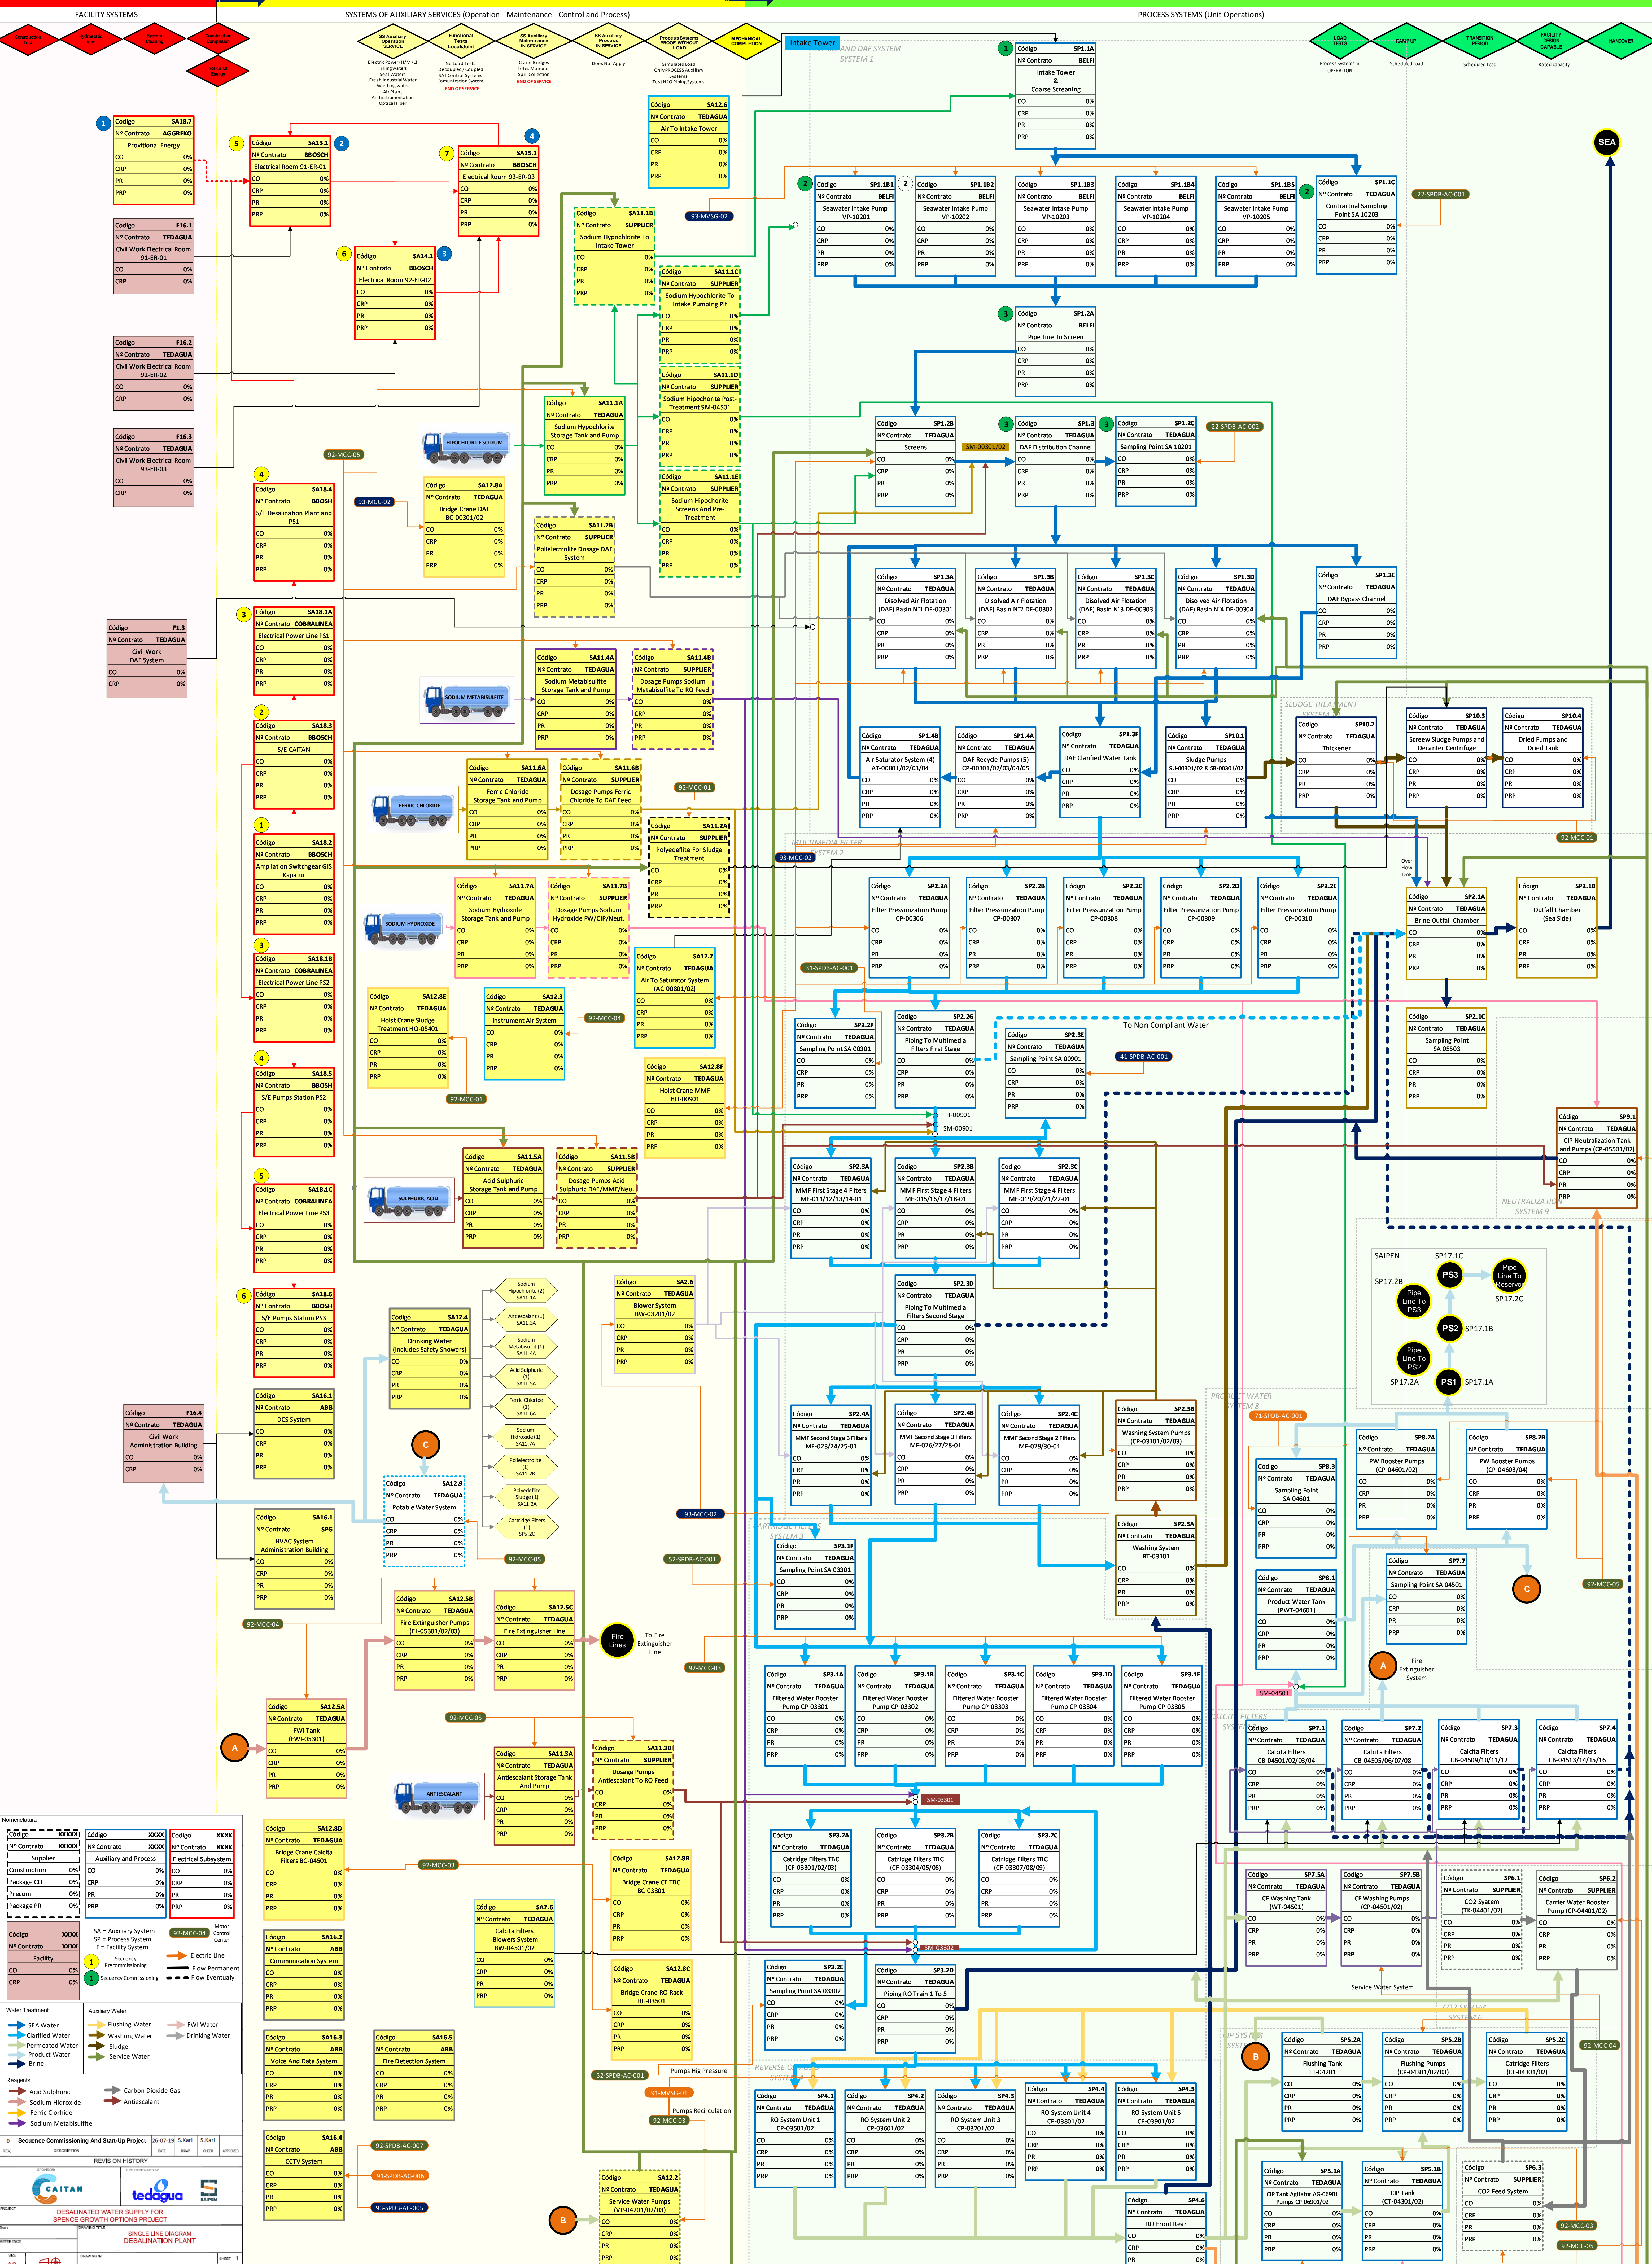

Item	Code	Description	CO	CRP	PR	PRP
SA18.2	XXXX	Provisional Energy				
F16.1	XXXX	Civil Work Electrical Room 91-ER-01				
F16.2	XXXX	Civil Work Electrical Room 92-ER-02				
F16.3	XXXX	Civil Work Electrical Room 93-ER-03				
F1.3	XXXX	Civil Work DAF System				

Item	Code	Description	CO	CRP	PR	PRP
SA18.1A	XXXX	Electrical Power Line PS1				
SA18.1B	XXXX	Electrical Power Line PS2				
SA18.1C	XXXX	S/E Pumps Station PS2				
SA18.1D	XXXX	S/E Pumps Station PS3				
SA18.1E	XXXX	S/E Pumps Station PS4				
SA18.1F	XXXX	S/E Pumps Station PS5				
SA18.1G	XXXX	S/E Pumps Station PS6				
SA18.1H	XXXX	S/E Pumps Station PS7				
SA18.1I	XXXX	S/E Pumps Station PS8				
SA18.1J	XXXX	S/E Pumps Station PS9				
SA18.1K	XXXX	S/E Pumps Station PS10				
SA18.1L	XXXX	S/E Pumps Station PS11				
SA18.1M	XXXX	S/E Pumps Station PS12				
SA18.1N	XXXX	S/E Pumps Station PS13				
SA18.1O	XXXX	S/E Pumps Station PS14				
SA18.1P	XXXX	S/E Pumps Station PS15				
SA18.1Q	XXXX	S/E Pumps Station PS16				
SA18.1R	XXXX	S/E Pumps Station PS17				
SA18.1S	XXXX	S/E Pumps Station PS18				
SA18.1T	XXXX	S/E Pumps Station PS19				
SA18.1U	XXXX	S/E Pumps Station PS20				
